Cody Drug

1505 S. Broadway St.

Sulphur Springs, TX 75482

Report # J122416

USP 797 Pharmacy Clean Room Compliancy Inspection

March 3, 2026

MEDICAL TECHNOLOGY ASSOCIATES

Questions or Problems Please Contact our office at (877) 569-8886 or corp@mtausa.com

(877) 569-8886
727-548-8600 Phone
727-548-8622 Fax

The Pharmacy Division of MTA, Inc. completed a Pharmacy Clean Room Compliancy Inspection at your facility. All testing will determine if the room meets or exceeds USP 797 code compliance and other applicable federal, state and local requirements.

The following Clean Room tests were performed and are reported:

- HEPA Filter Integrity Test
- Supply Air Flow Volumes
- Air Changes Per Hour
- Air Flow Analysis
- Room Pressures Differentials
- Airborne Particle Count Classification per ISO 14644-1 @ 0.5 microns
- Microbiological Analysis (Viable Count)

The test results documented within this report have not been modified or changed unless noted. Results are confidential and reported directly to the responsible staff members. If there are questions or concerns pertaining to the report we will be happy to arrange a meeting with you and/or your staff.

USP 797 CERTIFICATION EXECUTIVE SUMMARY

MEDICAL TECHNOLOGY ASSOCIATES

Date	March 3, 2026	Report Number	J122416
Technician	Angel Estrada		
Device ID#	20605.101		
Customer	Cody Drug		
Address	1505 S. Broadway St.		
City State	Sulphur Springs, TX 75482		

Contact	Will Douglas	/	
Telephone	903-885-2639	/	
email address	willdouglas@outlook.com	/	0
PO#		/	

Notes:

1 MTA Tech / 1 Pharmacy Tech

	Meets or Exceeds requirements of USP 797	Does NOT meet the requirements of USP 797	Non-Applicable
ISO8 Non-Haz Powder Room			
Particle Count Survey	X		
Differential Pressure	X		
Air Changes	X		
Ceiling HEPA Test	X		
ISO8 Gowning Room			
Particle Count Survey	X		
Differential Pressure	X		
Air Changes	X		
Ceiling HEPA Test	X		
ISO7 Non-Hazardous (IV Room)			
Particle Count Survey	X		
Differential Pressure	X		
Air Changes	X		
Ceiling HEPA Test	X		

*Executive summary does not include results of viable air samples.

Laminar Flow Hoods, Isolators, Biological Safety Cabinets	Pass	Fail	Requires Attention
SN# BSC.102 2024-205509	X		
SN# C-1 Pow. Hood SS 324-HEMS	X		
SN#			
SN#			
SN#			
SN#			

CUSTOMER NAME (PLEASE PRINT)

CUSTOMER SIGNATURE

Angel Estrada

AUTHORIZED SERVICE REP

March 3, 2026

DATE

CHAIN OF CUSTODY

Date	March 3, 2026	Time of Testing	10:00 AM
Report #	J122416		
Technician	Angel Estrada		
Customer	Cody Drug		
Address	1505 S. Broadway St.		
City State	Sulphur Springs, TX 75482		
Contact	Will Douglas /		
Telephone	903-885-2639		
Customer #	20605		

MEDICAL TECHNOLOGY ASSOCIATES

Toll Free	(877) 569-8886
Phone	(727) 548-8600
Fax	(727) 548-8622

www.mtausa.com

Occupancy State During Testing	Operational / Dynamic
Email Address to Send Report:	/
Email Address to Send Report:	willdouglas@outlook.com

Notes:

****DUAL INCUBATION*****

Media/Agar Type	Triptic Soy Agar		
Lot #	362000	Exp. Date	05-Apr-26
		MFG	Remel

Sample ID	Sample Location/ Device ID	ISO Class	Sample Volume
1	Control		
2	Powder Room	8	1000 L
3	Gowning Room	8	1000 L
4	IV Room	7	1000 L
5	BSC.102	5	1000 L
6			
7			
8			
9			
10			
11			
12			
13			

Media/Agar Type	Triptic Soy Agar		
Lot #	369855	Exp. Date	20-Apr-26
		MFG	Remel

Sample ID	Sample Location	ISO Class	Sample Volume
1	Control		
2	Powder Room Table	8	Surface
3	Gown Room Rack	8	Surface
4	IV Room Table	7	Surface
5	BSC.102	5	Surface
20			
21			
22			
23			
24			
25			
26			

Section 1

USP 797 Pharmacy

Ante Room, IV Room and Chemo Room Summary Reports

NON-HAZ-POWDER ROOM SUMMARY

Date	March 3, 2026
Report #	J122416
Device ID #	20605.101
Technician	Angel Estrada
Customer	Cody Drug
Address	1505 S. Broadway St.
City State	Sulphur Springs, TX 75482
Telephone	903-885-2639 /
Contact	Will Douglas
PO Number	

Overall Status of Room

ISO 14644-1 **2015** Class **8** at .5 micron Status **Operational**

Meets CETA CAG-003-2022	X	Pass		Fail		N/A
Meets USP 797 to Criteria Tested	X	Pass		Fail		N/A

Notes:

Air Change Requirements:

Minimum 30 air changes required for ISO 7 and 20 air changes for ISO 8

Total Air Volume Supplied	244	CFM	Total Number of Air Changes	23	per hour	X	Pass		Fail		N/A

Differential Pressure:

Minimum 0.02 inches positive to the outside area.

Pressure monitor Present?						X	YES		NO		N/A
Differential Pressure of Powder Room to Outside	0.022	"W.G.	or	N/A	fpm	X	Pass		Fail		N/A
Differential Pressure of Gown to Non-Class Room	0.082	"W.G.	or	N/A	fpm	X	Pass		Fail		N/A
Differential Pressure of IV Room to Gown Room	0.042	"W.G.	or	N/A	fpm	X	Pass		Fail		N/A
	N/A	"W.G.	or	N/A	fpm		Pass		Fail	X	N/A

Ante Room Statistical Data 0 .5 micron Particles:

(Particle counts taken at 1 minute sample time at 1 CFM and include 0.5 micron particles and larger)

Max UCL is used to determine ISO classification when nine (9) or less particle count locations are taken.

Maximum number of .5 micron size particles allowed for ISO Class 7	352,000	particles per cubic meter
Maximum number of .5 micron size particles allowed for ISO Class 8	3,520,000	particles per cubic meter

ISO Class Achieved	8	Mean of Averages	25897	Max	66967	X	Pass		Fail		N/A

HEPA Filter Leak Integrity Test:

Upstream concentration should be greater than 10µg/l and no leak greater than 0.01% when scanned. (See Data Page for more information.)

Number of filters scanned	2	Did any filters fail?		Yes	X	No	If yes is marked see drawing for individual status of each filter.				
Number of leaks detected	0										
Number of leaks sealed								Pass		Fail	X N/A

Average Temperature and Relative Humidity:

Recommended Temperature < 20° C	Measured	19.2	°C	(not mandatory for compliance)
Recommended Relative Humidity 35 to 65%	Measured	53.2	%Rh	(not mandatory for compliance)

Smoke Study Performed:

Visual confirmation that pressure differentials are consistent in the direction designed for the type of room.	X	Pass		Fail		N/A

Completed under Dynamic Conditions

GOWNING ROOM SUMMARY

MEDICAL TECHNOLOGY ASSOCIATES

Date	March 3, 2026
Report #	J122416
Device ID #	20605.101
Technician	Angel Estrada
Customer	Cody Drug
Address	1505 S. Broadway St.
City State	Sulphur Springs, TX 75482
Telephone	903-885-2639 /
Contact	Will Douglas
PO Number	

Overall Status of Room

ISO 14644-1 **2015** Class **8** at .5 micron Status **Operational**

Meets CETA CAG-003-2022	[X] Pass	[ ] Fail	[ ] N/A
Meets USP 797 to Criteria Tested	[X] Pass	[ ] Fail	[ ] N/A

Notes:

Air Change Requirements:

15 air changes must be from supply air

Air Changes for Room only (15 required)	42 per hour	[X] Pass	[ ] Fail	[ ] N/A

Differential Pressure:

Minimum 0.02 inches positive to the ante area or any other area.

Pressure monitor Present?				[X] YES	[ ] NO	[ ] N/A
Differential Pressure of Gown Room to Non-Class Room	0.082 "W.G.	or	N/A fpm	[X] Pass	[ ] Fail	[ ] N/A
Differential Pressure of IV Room to Gown Rm	0.042 "W.G.	or	N/A fpm	[X] Pass	[ ] Fail	[ ] N/A
N/A				[ ] Pass	[ ] Fail	[X] N/A

Gown Room Statistical Data 0 .5 micron Particles: (Particle counts taken at 1 minute sample time at 1 CFM and include 0.5 micron particles and larger)

Max UCL is used to determine ISO classification when nine (9) or less particle count locations are taken.

Maximum number of .5 micron size particles allowed for ISO Class 7 352,000 particles per cubic meter

ISO Class Achieved	8	Mean of Averages	3232	Max	3780	[X] Pass	[ ] Fail	[ ] N/A

HEPA Filter Leak Integrity Test:

Upstream concentration should be greater than 10µg/l and no leak greater than 0.01% when scanned. (See Data Page for more information.)

Number of filters scanned	1
Number of leaks detected	0
Number of leaks sealed	

Did any filters fail? [ ] Yes [X] No — If yes is marked see drawing for individual status of each filter.

[X] Pass [ ] Fail [ ] N/A

Average Temperature and Relative Humidity:

Recommended Temperature < 20° C	Measured	18.5 °C	(not mandatory for compliance)
Recommended Relative Humidity 35 to 65%	Measured	51.5 %Rh	(not mandatory for compliance)

Smoke Study Performed:

Visual confirmation that pressure differentials are consistent in the direction designed for the type of room. [X] Pass [ ] Fail [ ] N/A

Completed under Dynamic Conditions

NON-HD IV ROOM SUMMARY

MEDICAL TECHNOLOGY ASSOCIATES

Date	March 3, 2026
Report #	J122416
Device ID #	20605.101
Technician	Angel Estrada
Customer	Cody Drug
Address	1505 S. Broadway St.
City State	Sulphur Springs, TX 75482
Telephone	903-885-2639 /
Contact	Will Douglas
PO Number	

Overall Status of Room

ISO 14644-1 **2015** Class **7** at .5 micron Status **Operational**

Meets CETA CAG-003-2022	[X] Pass	[ ] Fail	[ ] N/A
Meets USP 797 to Criteria Tested	[X] Pass	[ ] Fail	[ ] N/A

Notes:

Air Change Requirements:

15 air changes must be from supply air	Air Changes for Room only (15 required)	113	per hour	[X] Pass	[ ] Fail	[ ] N/A
Air changes allowed from PEC	Air Changes from PEC only	85	per hour			
Minimum 30 air changes required for ISO 7	Total Number of Air Changes	198	per hour	[X] Pass	[ ] Fail	[ ] N/A

Differential Pressure:

Minimum 0.02 inches positive to the ante area or any other area.

Pressure monitor Present?					[X] YES	[ ] NO	[ ] N/A
Differential Pressure of IV Room to Gown Room	0.082	"W.G. or	N/A	fpm	[X] Pass	[ ] Fail	[ ] N/A
Differential Pressure of IV Room to Outside	N/A	"W.G. or	N/A	fpm	[ ] Pass	[ ] Fail	[X] N/A
	N/A				[ ] Pass	[ ] Fail	[X] N/A

IV Room Statistical Data 0 .5 micron Particles:

(Particle counts taken at 1 minute sample time at 1 CFM and include 0.5 micron particles and larger)

Max UCL is used to determine ISO classification when nine (9) or less particle count locations are taken.

Maximum number of .5 micron size particles allowed for ISO Class 7 352,000 particles per cubic meter

ISO Class Achieved	7	Mean of Averages	1819	Max	2649	[X] Pass	[ ] Fail	[ ] N/A

HEPA Filter Leak Integrity Test:

Upstream concentration should be greater than 10µg/l and no leak greater than 0.01% when scanned. (See Data Page for more information.)

Number of filters scanned	3	Did any filters fail?	[ ] Yes	[X] No	If yes is marked see drawing for individual status of each filter.
Number of leaks detected	0				
Number of leaks sealed			[X] Pass	[ ] Fail	[ ] N/A

Average Temperature and Relative Humidity:

Recommended Temperature < 20° C	Measured	17.8	°C	(not mandatory for compliance)
Recommended Relative Humidity 35 to 65%	Measured	51.5	%Rh	(not mandatory for compliance)

Smoke Study Performed:

Visual confirmation that pressure differentials are consistent in the direction designed for the type of room. [X] Pass [ ] Fail [ ] N/A

Completed under Dynamic Conditions

Section 2

USP 797 Pharmacy

Report Data Includes Calibration Data

CLEANROOM INSPECTION DATA

Date	March 3, 2026	Time	10:00 AM
Technician	Angel Estrada		
Device ID#	20605.101		
Customer	Cody Drug		
Address	1505 S. Broadway St.		
City State	Sulphur Springs, TX 75482		

MEDICAL TECHNOLOGY ASSOCIATES

Report Number	J122416
Contact	Will Douglas /
Telephone	903-885-2639 /
email address	willdouglas@outlook.com /
PO#	

NON-HAZ POWDER ROOM DIMENSIONS AND PARTICLE COUNT STATISTICAL DATA

Room Dimensions recorded in inches — Non-applicable

L	W	H		Value	Unit	Calculations
152	76	97	Room Area in square feet ft²	80.22	ft²	(Length (in) X width (in)) x 1 ft²/144 in²
			Room Area in square meters (m²)	7.45	m²	area (ft²) x 1 m²/10.764 ft²
			Room Volume in cubic feet (ft³)	648.46	ft³	(Length (in) X width (in) x Height (in) x 1 ft³/1728 in³
			Number of Sampling Locations	4		Compare Area to Chart ISO 14644 rev 2015

Ante Room Particle Count Statistical Data (Particle counts taken at 1 minute sample time at 1 CFM and include 0.5 micron particles and larger)

ISO Class	Mean of Averages	Max	Standard Dev	Standard Err.
8	25897	66967	27822	N/A

GOWNING ROOM DIMENSIONS AND PARTICLE COUNT STATISTICAL DATA

Room Dimensions recorded in inches — Non-applicable

L	W	H		Value	Unit	Calculations
68	88	97	Room Area in square feet ft²	41.56	ft²	(Length (in) X width (in)) x 1 ft²/144 in²
			Room Area in square meters (m²)	3.86	m²	area (ft²) x 1 m²/10.764 ft²
			Room Volume in cubic feet (ft³)	335.91	ft³	(Length (in) X width (in) x Height (in) x 1 ft³/1728 in³
			Number of Sampling Locations	2		Compare Area to Chart ISO 14644 rev 2015

GOWN Room Particle Count Statistical Data (Particle counts taken at 1 minute sample time at 1 CFM and include 0.5 micron particles and larger)

ISO Class	Mean of Averages	Max	Standard Dev	Standard Err.
8	3232	3780	774	N/A

IV ROOM DIMENSIONS AND PARTICLE COUNT STATISTICAL DATA

Room Dimensions recorded in inches — Non-applicable

L	W	H		Value	Unit	Calculations
68	88	97	Room Area in square feet ft²	41.56	ft²	(Length (in) X width (in)) x 1 ft²/144 in²
			Room Area in square meters (m²)	3.86	m²	area (ft²) x 1 m²/10.764 ft²
			Room Volume in cubic feet (ft³)	335.91	ft³	(Length (in) X width (in) x Height (in) x 1 ft³/1728 in³
			Number of Sampling Locations	2		Compare Area to Chart ISO 14644 rev 2015

IV Room Particle Count Statistical Data (Particle counts taken at 1 minute sample time at 1 CFM and include 0.5 micron particles and larger)

ISO Class	Mean of Averages	Max	Standard Dev	Standard Err.
7	1819	2649	1174	N/A

AIR SUPPLY VOLUME MEASUREMENT DATA

[X] Direct Measurement Method [ ] Velgrid Measurement Method/Multi point array [ ] Single point / velometer method

Calculate K factor for a filter when DIM cannot be measured: HEPA filter # ____ HEPA Filter Face Area ____ Measured CFM ____ Measured FPM ____

(K-Factor = measured cfm/calculated cfm) Calculated CFM ____ K-factor ____

Non-Haz Powder Room

HEPA Filter # / Diffuser	#	Location	L	W	D	Sqft.	K Factor	FPM	CFM
HEPA Filter # / Diffuser	1	Powder /Ante Rm	24	24		3.4			124
HEPA Filter # / Diffuser	2	Powder /Ante Rm				0.0			120
HEPA Filter # / Diffuser						0.0			

Gowning Room

HEPA Filter # / Diffuser	#	Location	L	W	D	Sqft.	K Factor	FPM	CFM
HEPA Filter # / Diffuser	3	Gown Rm	24	24		3.4			234
HEPA Filter # / Diffuser									
HEPA Filter # / Diffuser									

IV Room

HEPA Filter # / Diffuser	#	Location	L	W	D	Sqft.	K Factor	FPM	CFM
HEPA Filter # / Diffuser	4	IV Rm	24	24		3.4		120.0	163
HEPA Filter # / Diffuser	5	IV Rm	24	24		3.4			247
HEPA Filter # / Diffuser	6	IV Rm	24	24		3.4			222

Report Number J122416

AIR CHANGE AND PRESSURE DATA

Non-Haz Powder Room

Room Volume	648	Supply Air Total	244	Air Changes Per minute	0.38	Air Changes Per Hour	23
Total Air Volume from PEC		Total Air Volume		Total Air changes Per hour with PEC		X	**Non-applicable**

Notes:

Gowning Room

Room Volume	336	Supply Air Total	234	Air Changes Per minute	0.70	Air Changes Per Hour	42
Total Air Volume from PEC	N/A	Total Air Volume	N/A	Total Air changes Per hour with PEC	N/A	X	**Non-applicable**

Notes:

IV Room

Room Volume	336	Supply Air Total	632	Air Changes Per minute	1.88	Air Changes Per Hour	113
Total Air Volume from PEC	475	Air Changes from PEC	85	Total Air changes Per hour with PEC	198	X	**Non-applicable**

Notes:

Pressure/Velocity Monitors Installed?	X YES	NO	N/A
Pressure monitor Installed and Functioning?	X YES	NO	N/A

Differential Pressure Pow / Ante to Outside	0.022 "W.G.	Differential Pressure Gown Rm to Pow / Non-Clas	0.082 "W.G.	Differential Pressure IV to Gown Rm	0.042 "W.G.		
Differential Pressure to		measured	"W.G.	Differential Pressure to		measured	"W.G.

HEPA FILTER INTEGRITY TEST

(HEPA filters should be integrity tested at each certification with a minimum upstream challenge concentration of 10 micrograms per liter.)

Powder / Non-Classified Room

HEPA Filter #		Upstream Challenge Location	Calculated Challenge	Measured challenge Before	Measured challenge After	Leak Detected Yes	Leak Detected No	Leak Sealed Yes	Leak Sealed No
HEPA Filter #	1	Ceiling Port in Room	54				X		
HEPA Filter #	2	Ceiling Port in Room	56				X		
HEPA Filter #	0								

Gowning Room

HEPA Filter #		Upstream Challenge Location	Calculated Challenge	Measured challenge Before	Measured challenge After	Leak Detected Yes	Leak Detected No	Leak Sealed Yes	Leak Sealed No
HEPA Filter #	3	Ceiling Port in Room	58				X		
HEPA Filter #	0								
HEPA Filter #	0								
HEPA Filter #	0								

IV Room

HEPA Filter #		Upstream Challenge Location	Calculated Challenge	Measured challenge Before	Measured challenge After	Leak Detected Yes	Leak Detected No	Leak Sealed Yes	Leak Sealed No
HEPA Filter #	4	Ceiling Port in Room	83				X		
HEPA Filter #	5	Ceiling Port in Room	55				X		
HEPA Filter #	6	Ceiling Port in Room	61				X		
HEPA Filter #	0								

Report Number	J122416

ADDITIONAL DATA

Average Noise Level	N/A	dBA	Pow / Ante Rm Average Temperature	19.2	°C	Ante Rm Average Relative Humidity Level	53.2	%Rh
Average Noise Level	N/A	dBA	Gown Rm Average Temperature	18.5	°C	IV Buffer Average Relative Humidity Level	51.5	%Rh
Average Noise Level	N/A	dBA	IV Buffer Rm Average Temperature	17.8	°C	IV Buffer Average Relative Humidity Level	52.2	%Rh

Ceiling tiles sealed down/gasketed?	X YES	NO	N/A
Floors have coved edges and corners?	X YES	NO	N/A
Drawing of room complete?	X YES	NO	N/A
Profile of Viable Sample Locations Complete?	X YES	NO	N/A
Profile of Particle Count Locations Complete?	X YES	NO	N/A
Profile of Room HEPA Filters, Leak/Patches and challenge induction points complete?	X YES	NO	N/A
Profile of Room Pressures Complete?	X YES	NO	N/A
Profile of Room Air Supply / Return Complete?	X YES	NO	N/A
Profile of Temperature and Humidity Readings Complete?	X YES	NO	N/A

VERIFICATION OF PRESSURE MONITORS

Date	March 3, 2026
Report #	J122416
Technician	Angel Estrada
Customer	Cody Drug
Address	1505 S. Broadway St.
City State	Sulphur Springs, TX 75482
Contact	Will Douglas
Telephone	903-885-2639
Customer #	20605

MEDICAL TECHNOLOGY ASSOCIATES

Toll Free	(877) 569-8886
Phone	(727) 548-8600
Fax	(727) 548-8622

www.mtausa.com

Notes:

Gage ID	Description or ID#	SN# or other Discription	Range	Adjustment	Reading As Found	Calibrated Source Reading			Calibrated Average	Reading as Left	
						1	2	3			
1	Pow Rm to outside	Digital	0 - 0.25	No	0.022	0.0216	0.0227	0.0226	0.0223	0.022	"W.G
2	Gown to Pow Rm	Digital	0 - 0.25	No	0.04	0.0816	0.082	0.0816	0.0817	0.04	"W.G
3	IV to Gown	Digital	0 - 0.25	No	0.04	0.0419	0.0418	0.0414	0.0417	0.04	"W.G
									N/A		"W.G
									N/A		"W.G
									N/A		"W.G

Medical Technology Associates, Inc.
6651 102nd Ave. N., Pinellas Park, FL
33782
Toll Free: 877-569-8886
Fax: 727-548-8622

The list below is a list of the equipment that the MTA technician has on hand for use while performing work at your facility. Some of the equipment may or may not have been utilized. All instruments are calibrated by the manufacturer or other qualified vendor at least on an annual basis. All the instruments have been calibrated using Calibration Standards which are NIST (National Institute of Standards and Technology) traceable. If you need copies of the actual calibration certificate please contact our corporate office at: (877) 569-8886 or corp@mtausa.com

Technician	Angel Estrada

CALIBRATION DATA

Equipment	Manufacturer	Model #	Serial #	Calibration Date	Calibration Due
Particle Counter	Particle Measuring Systems	Lasair 310c	139173	Jan-26	Jan-27
Hot Wire / Velometer	TSI	9545-A	9545A2405006	Nov-25	Nov-26
Aerosol Photometer	TEC Services	PH-4	2184	Apr-25	Apr-26
Air Volume Capture hood	ALNOR	EBT-721	EBT731949018	Mar-25	Mar-26
Air Sampler	Bio-Culture / Buck	B30120	C103225	Daily	Daily
Air Sampler	Bio-Culture / Buck	B30120	C103226	Daily	Daily
Bio-Culture Calibrator	Bio-Culture Calibrator	2000-6MM	W48AEMB-250	May-25	May-26
ASTM Weights	Troemner				

Section 3

USP 797 Pharmacy

Hood Reports

Biological Safety Cabinet Certification Report

Date	March 3, 2026
Report #	J122416 -2
Technician	Angel Estrada
Customer	Cody Drug
Address	1505 S. Broadway St.
City State	Sulphur Springs, TX 75482
Contact	Will Douglas
Telephone	903-885-2639
PO Number	

MEDICAL TECHNOLOGY ASSOCIATES

Overall Status [X] Pass [ ] Fail

[ ] **Requires Attention**

Device ID#	20605.102
Manufacturer	ESCO
Model	AC2-4S9-NS G4 8"
Serial Number	2024-205509
Device Location	IV / Buffer Room

Notes:

ACCEPTANCE CRITERIA

Inflow / Face Velocity Tests 100 - 110 | Inflow Velocity 103 fpm.

Downflow / Supply Velocity 60 - 70 | Downflow Velocity 67 fpm.

Individual point readings should be within +/- 25% or 16 fpm whichever is greater.

Individual Readings 51 Low 83 High | 57 Low 76 High

HEPA Filter Leak Test

Minimum challenge of 10 micrograms per liter. No leak should exceed 0.01% when scanned or 0.005% when probed.

Upstream Concentration	18	µg/l
Number of leaks Detected	0	
Number of leaks Sealed		

Particulate Matter Profile (Particle counts taken at 1 minute sample time at 1 CFM and include 0.5 micron particles and larger)

Maximum number of .5 micron size particles and above allowed for ISO Class 5 is 3520 particles per cubic meter

ISO Class Achieved **5**

Static Pressure Readings NA "W.G | Duct Pressure N/A "W.G Measured Downstream

Air Flow Smoke Pattern Test

Downflow Test, View Screen Retention Test, Sash Seal Containment Test and Work Access Opening Retention Test.

Site Assessment Test

- Window Sash Alarm
- Negative Pressure visualization at exhaust canopy.
- Air Flow Alarms and Interlocks

FINAL RESULTS

Test	Pass	Fail	N/A
Inflow / Face Velocity Tests	X		
Downflow /Supply Velocity Tests	X		
HEPA Filter Integrity Test	X		
Particulate Matter Profile	X		
Air Flow Smoke Pattern Test	X		
Site Assessment Test – Window Sash Alarm	X		
Negative Pressure visualization at exhaust canopy			X
Air Flow Alarms and Interlocks			X

INSPECTION DATA

Equipment Data

Type of Cabinet: [ ] A1 (75 fpm inflow) [X] A2 [ ] B1 [ ] B2 [ ] Class I / Powder Hood

Exhaust Configuration: [X] Room [ ] No Blower [ ] Thimble [ ] Hard Connect [ ] Aux Blower [ ] Total Exhaust

	Supply HEPA Filter		Exhaust Filter	
Filter Size	(1) 18 X 47.25 X 2.62		(1) 24 ` 18 X 3.62	
Supply / Exhaust Area	7.11	sq.ft.	2.44	sq.ft.
Supply / Exhaust Velocity	67	fpm.	274	fpm.
Volume	475	cfm.	276	cfm.

Total Volume 751 cfm.

Work Access Opening Dimensions 8 Height 48.00 Width — Work Access Opening Area: 2.67 sq.ft.

[ ] Exhaust Method Range 65 - 76 [X] DIM Range 267 - 293 [ ] Restricted Access Range 109 - 120

Notes:

Downflow/Supply Velocity Readings 6 inch grid

59	57	58	62	62	61	59
67	64	68	68	68	67	70
71	70	73	75	74	76	75

Average 67

Exhaust, Traverse or Dim Readings 4 inch grid

271	270	278	274	277

Average 274

HEPA Filter Integrity Test

Zero Leaks | Zero Leaks

Particulate Matter Profile [ ] N/A

#1	#2	#3
0	0	0
Max	Mean	Std.D.
0	0	0

SUMMARY

MTA warrants that this air system was tested under the requirements as set forth in the following applicable standard(s):

[ ] IES-RP-CC-002.2; Heap Filters [X] NSF 49: Class II LAF Biosafety Cabinetry Annex F [X] CETA CAG 003-2022

[X] Manufacturer's Specifications [X] ISO 14644- **1** 2015; Class 5 at **0.5** um size particle, Status **Dynamic**

Status of System after Inspection:

[X] Certified to the Above Applicable Standard(s). [ ] Undergoing Corrective Action by MTA.

[ ] Not Certified to the Above Applicable Standard(s). [ ] It is Recommended that this System be Corrected by the Owner Prior to any Additional Testing.

CERTIFICATE OF INSPECTION' expires **6** months from date of issue.

*indicates duct area

Capture /Fume Hood Certification Report

Date	March 3, 2026
Report #	J122416 -3
Technician	Angel Estrada
Customer	Cody Drug
Address	1505 S. Broadway St.
City State	Sulphur Springs, TX 75482
Contact	Will Douglas
Telephone	903-885-2639
Email	

MEDICAL TECHNOLOGY ASSOCIATES

Overall Status [X] Pass [ ] Fail

[ ] Requires Attention

Device ID#	4018.103
Manufacturer	Sentry Air System
Model	76149-N-X
Serial Number	SS 324-HEMS
Device Location	ISO8 Powder Room

Notes:

Customer wants hood certified every 6 months

ACCEPTANCE CRITERIA

Inflow Velocity Profile

Inflow Velocity with sash at 8 " inches

Inflow Velocity 60+ -

Inflow Velocity Avg 167 fpm.

Comparative Value (Last Test) fpm

Air Flow Monitor

Ensure airflow alarms are functioning correctly and calibrate if necessary

Smoke Test

Visual Verification of that the smoke flows inward and does not reflux or escape and is not disturbed by equipment when passed along the bottom of the sash, the sash air foil, 1 inch inside the sash.

Visual Verification that cross drafts do not impact the flow of smoke at the sash opening

Physical Inspection

When accessible visual inspection of cables, pulleys and rollers for proper operation.

HEPA Filter Leak Test

No leak should exceed 0.005% when probed.

Upstream Concentration	N/A	Number of leaks Detected	0
Calculated Upstream Concentration	100	Number of leaks Sealed	

FINAL RESULTS

Inflow Velocity Test

[X] Pass [ ] Fail [ ] N/A

Air Flow Monitor Check

[ ] Pass [ ] Fail [X] N/A

Smoke Tests

[X] Pass [ ] Fail [ ] N/A

[X] Pass [ ] Fail [ ] N/A

Physical Inspection

[ ] Pass [ ] Fail [X] N/A

HEPA Filter Leak Test

[X] Pass [ ] Fail [ ] N/A

INSPECTION DATA

Equipment Data

	Round Duct		Rectangular Duct			Exhaust HEPA	
1. Duct Dimensions	Inches		X	[X] non-applicable	(2) 12 X 12 X 3	[ ] non-applicable	
2. Duct Area		sq.ft.				sq.ft.	
3. Maximum Access Opening Area		sq.ft.		Pre filters	1.33	sq.ft.	
4. Inflow Velocity		fpm.		) X X	167	fpm	
5. Volume		cfm.			222	cfm.	
6. Maximum Work Access Opening Dimensions:				Height 8	Width 24		

System Configuration

[ ] Fume Hood [ ] Capture Hood [ ] Surface/velocity slots [ ] Vent Tube

[X] Class I hood [ ] Dedicated Exhaust [ ] Multiple Exhaust / ganged hood number ____ of ____

Inflow Velocity Profile in fpm.

Sash Location: N/A	Sash Location: 8 "
	148 173 160 186
Average Inflow Velocity N/A	Average Inflow Velocity 167

SUMMARY

MTA warrants that this air system was tested under the requirements as set forth in the following applicable standard(s):

[ ] IES-RP-CC-002.2; HEPA Filters [X] ANSI Z 9.5: Laboratory Ventilation section 5.6.2 and 5.7.0 only [ ] Comparative Values

[X] Manufacturer's Specifications [ ] SEFA 1 [ ] Owners Specifications ____________________

Status of System after Inspection:

[X] Certified to the Above Applicable Standard(s). [ ] Undergoing Corrective Action by MTA.

[ ] Not Certified to the Above Applicable Standard(s). [ ] It is Recommended that this System be Corrected by the Owner Prior to any Additional Testing.

CERTIFICATE OF INSPECTION' expires **6** months from date of issue.

Section 4

USP 797 Pharmacy

Drawings

Report Number	J122416

Particulate Matter Profile

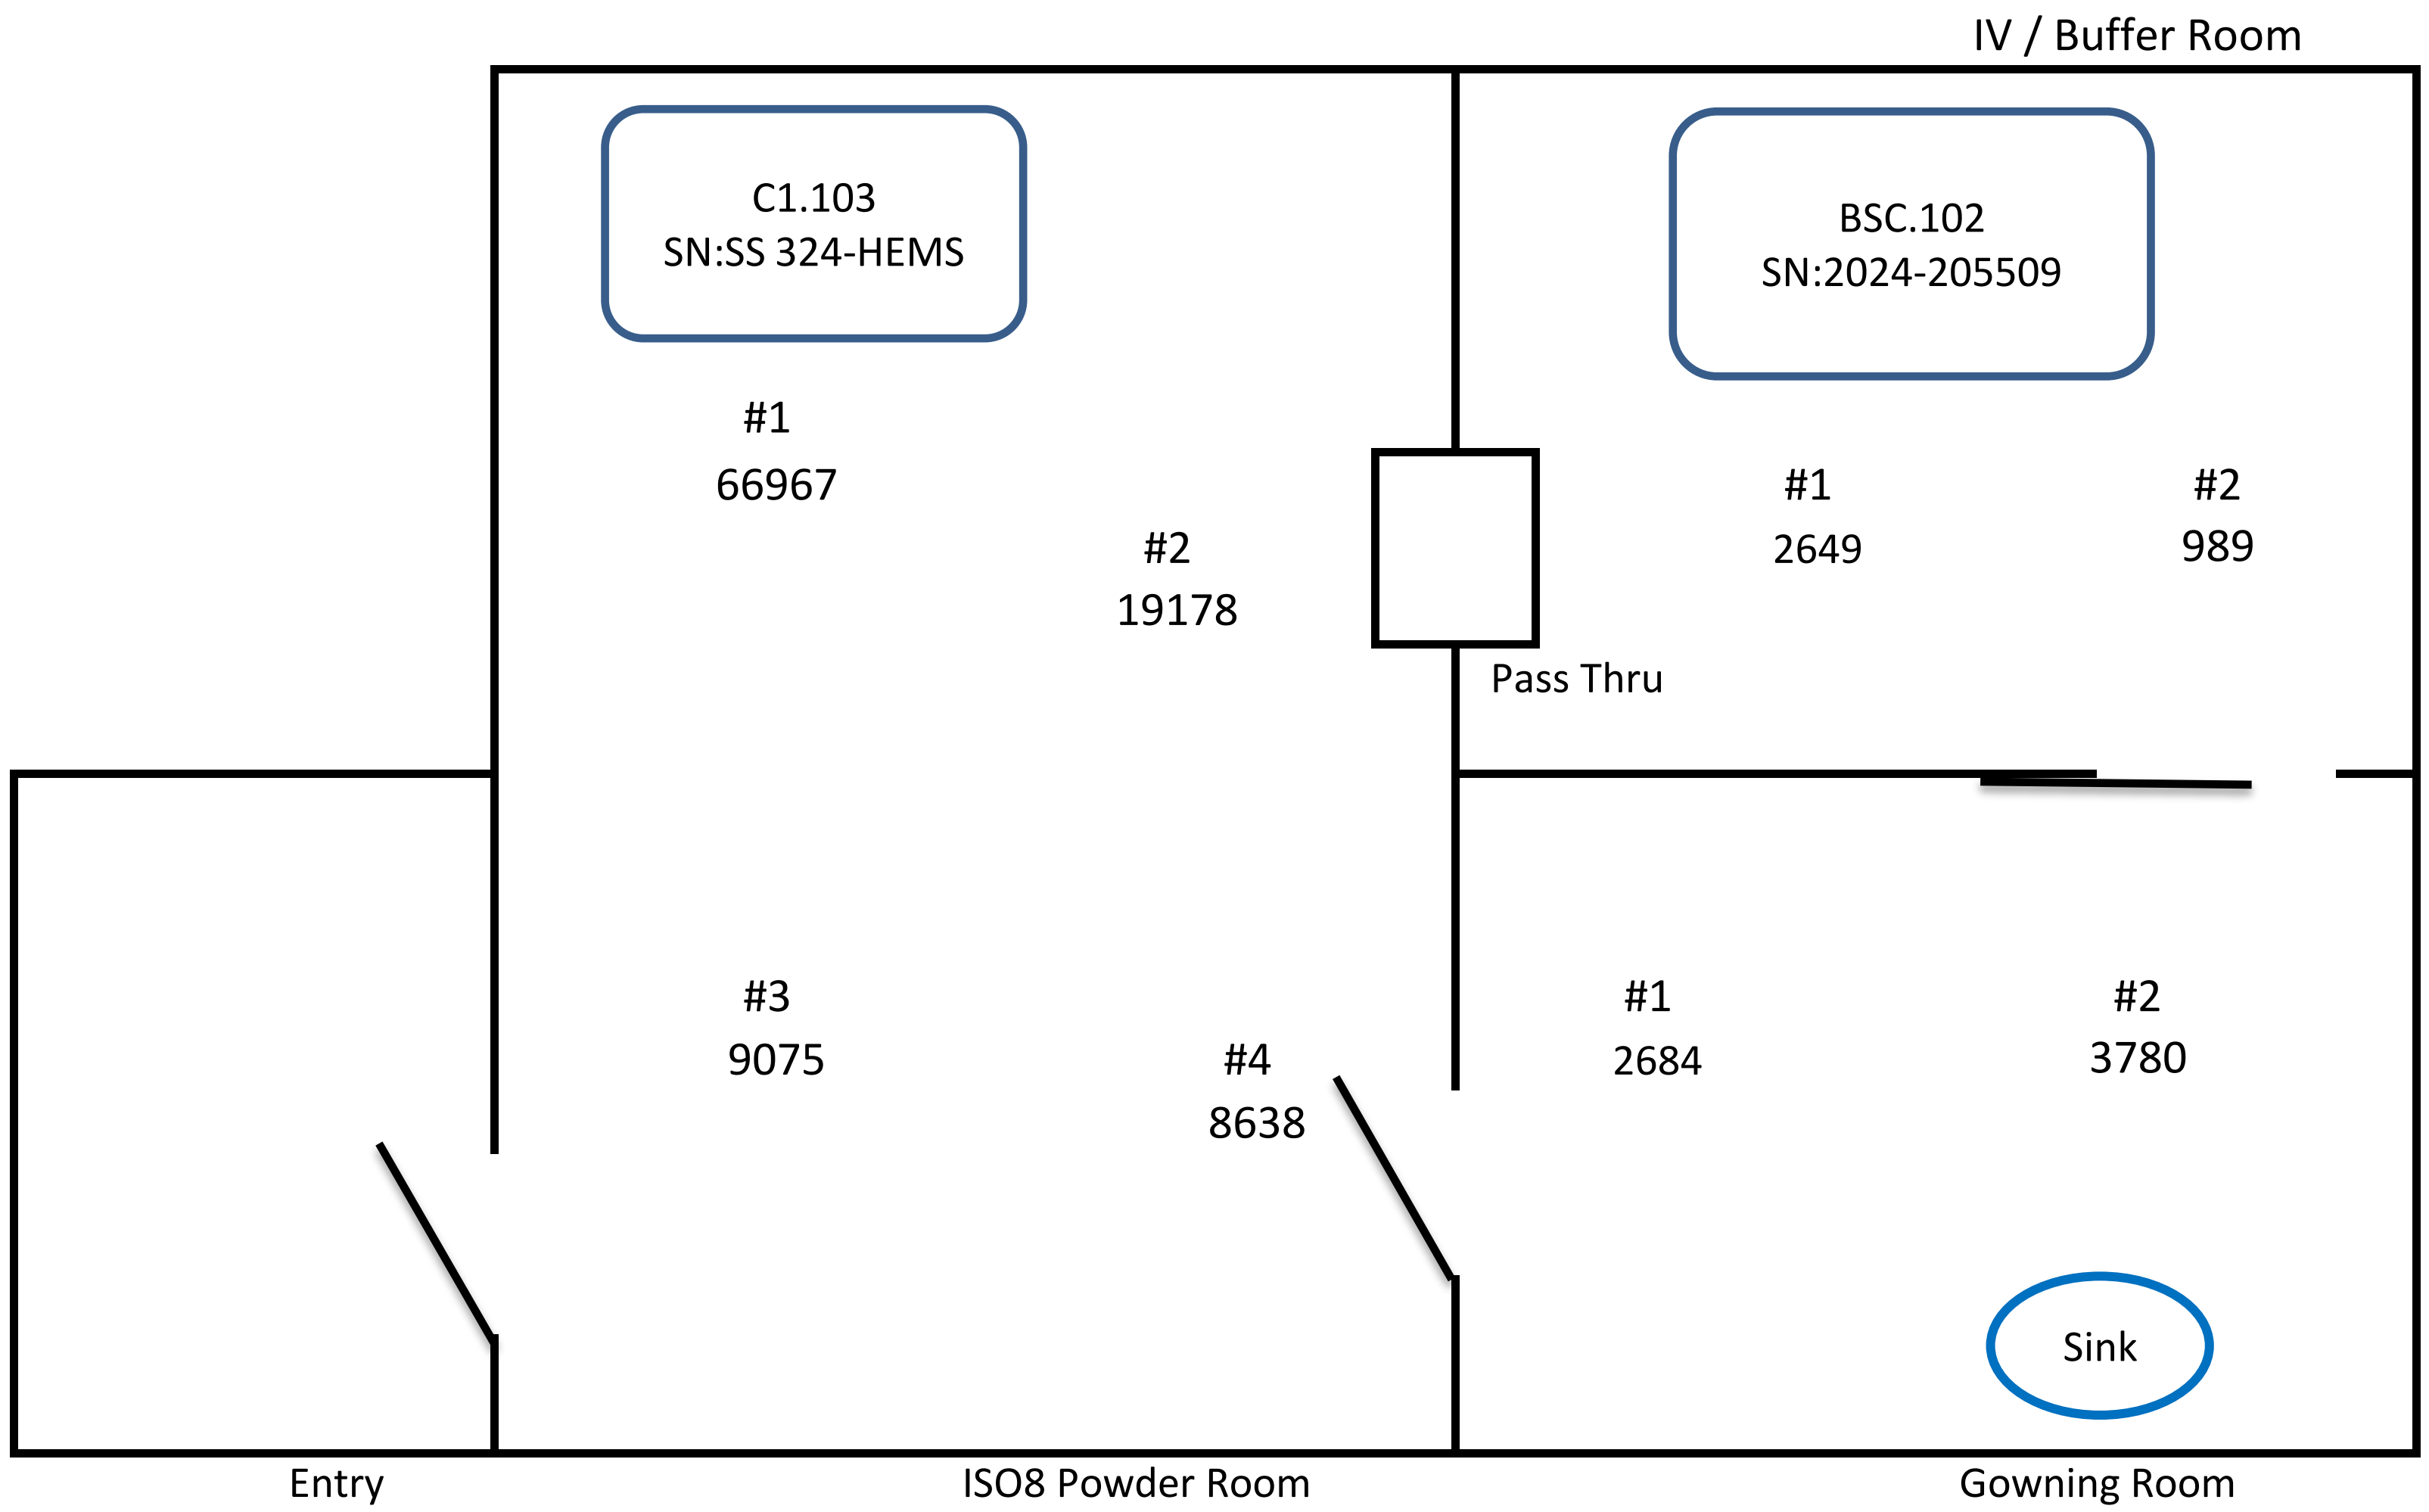

Temperature, Humidity, Supply and Pressure Profile

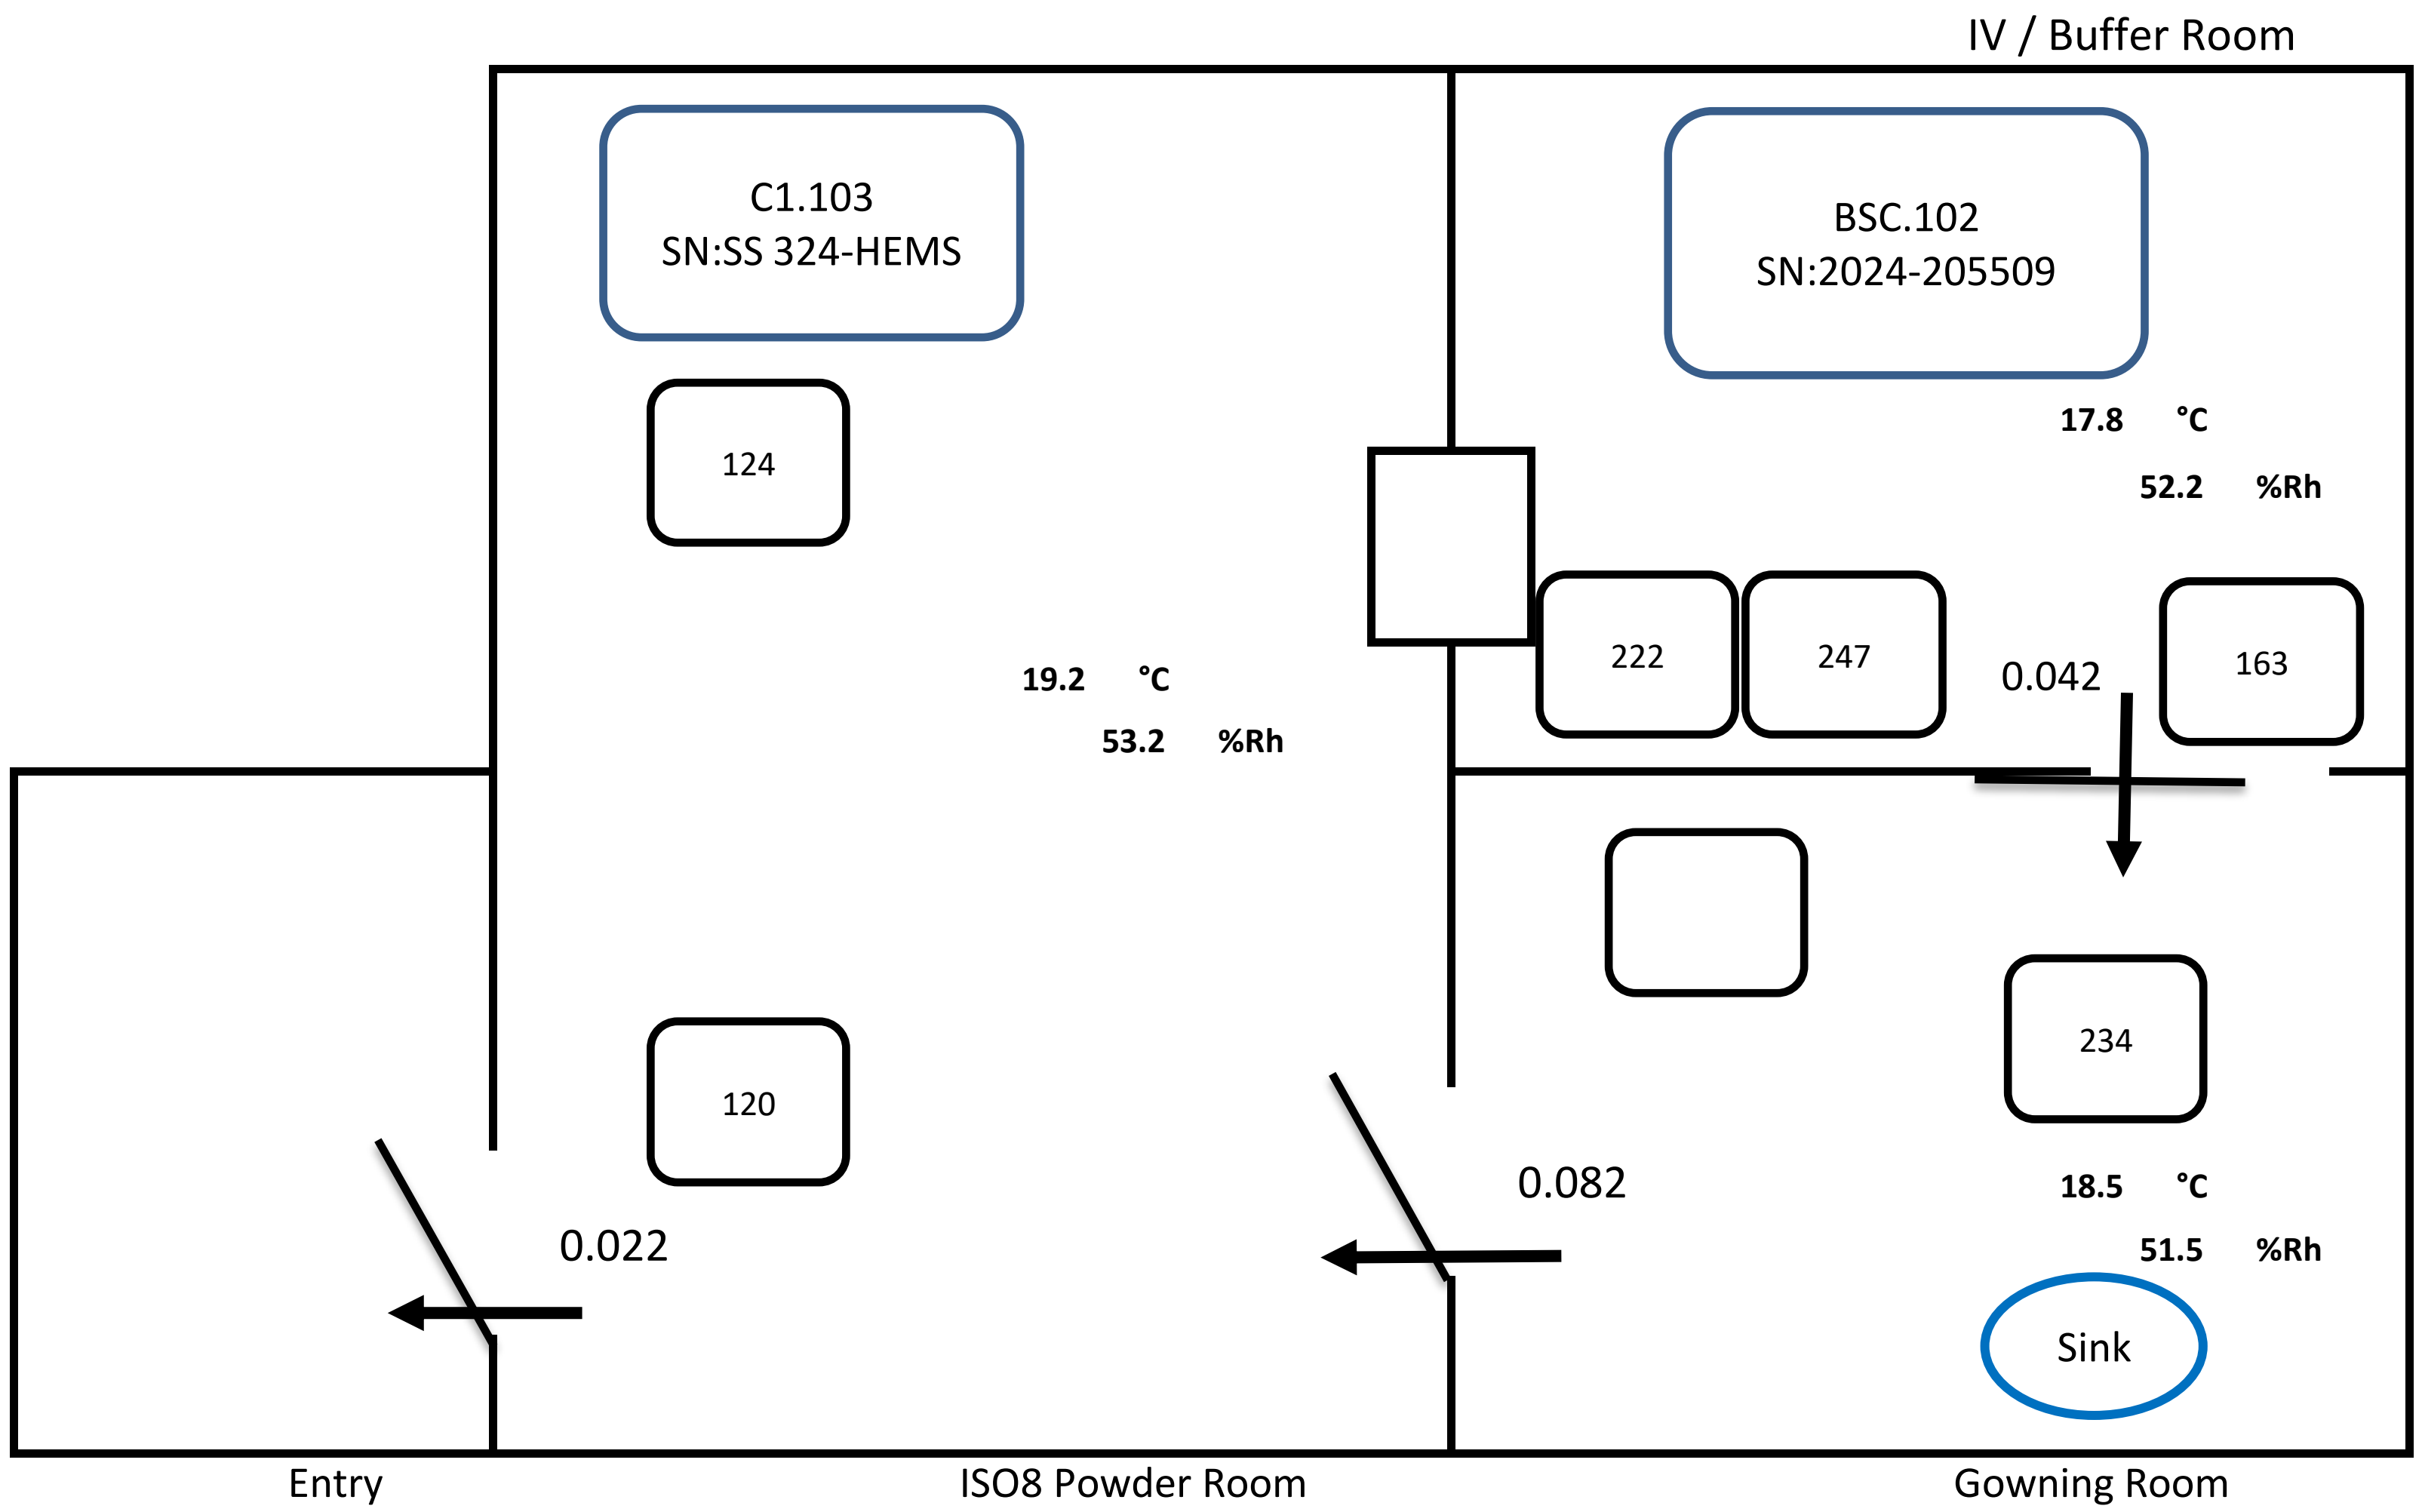

Report Number	J122416

Viable Air Sample Profile

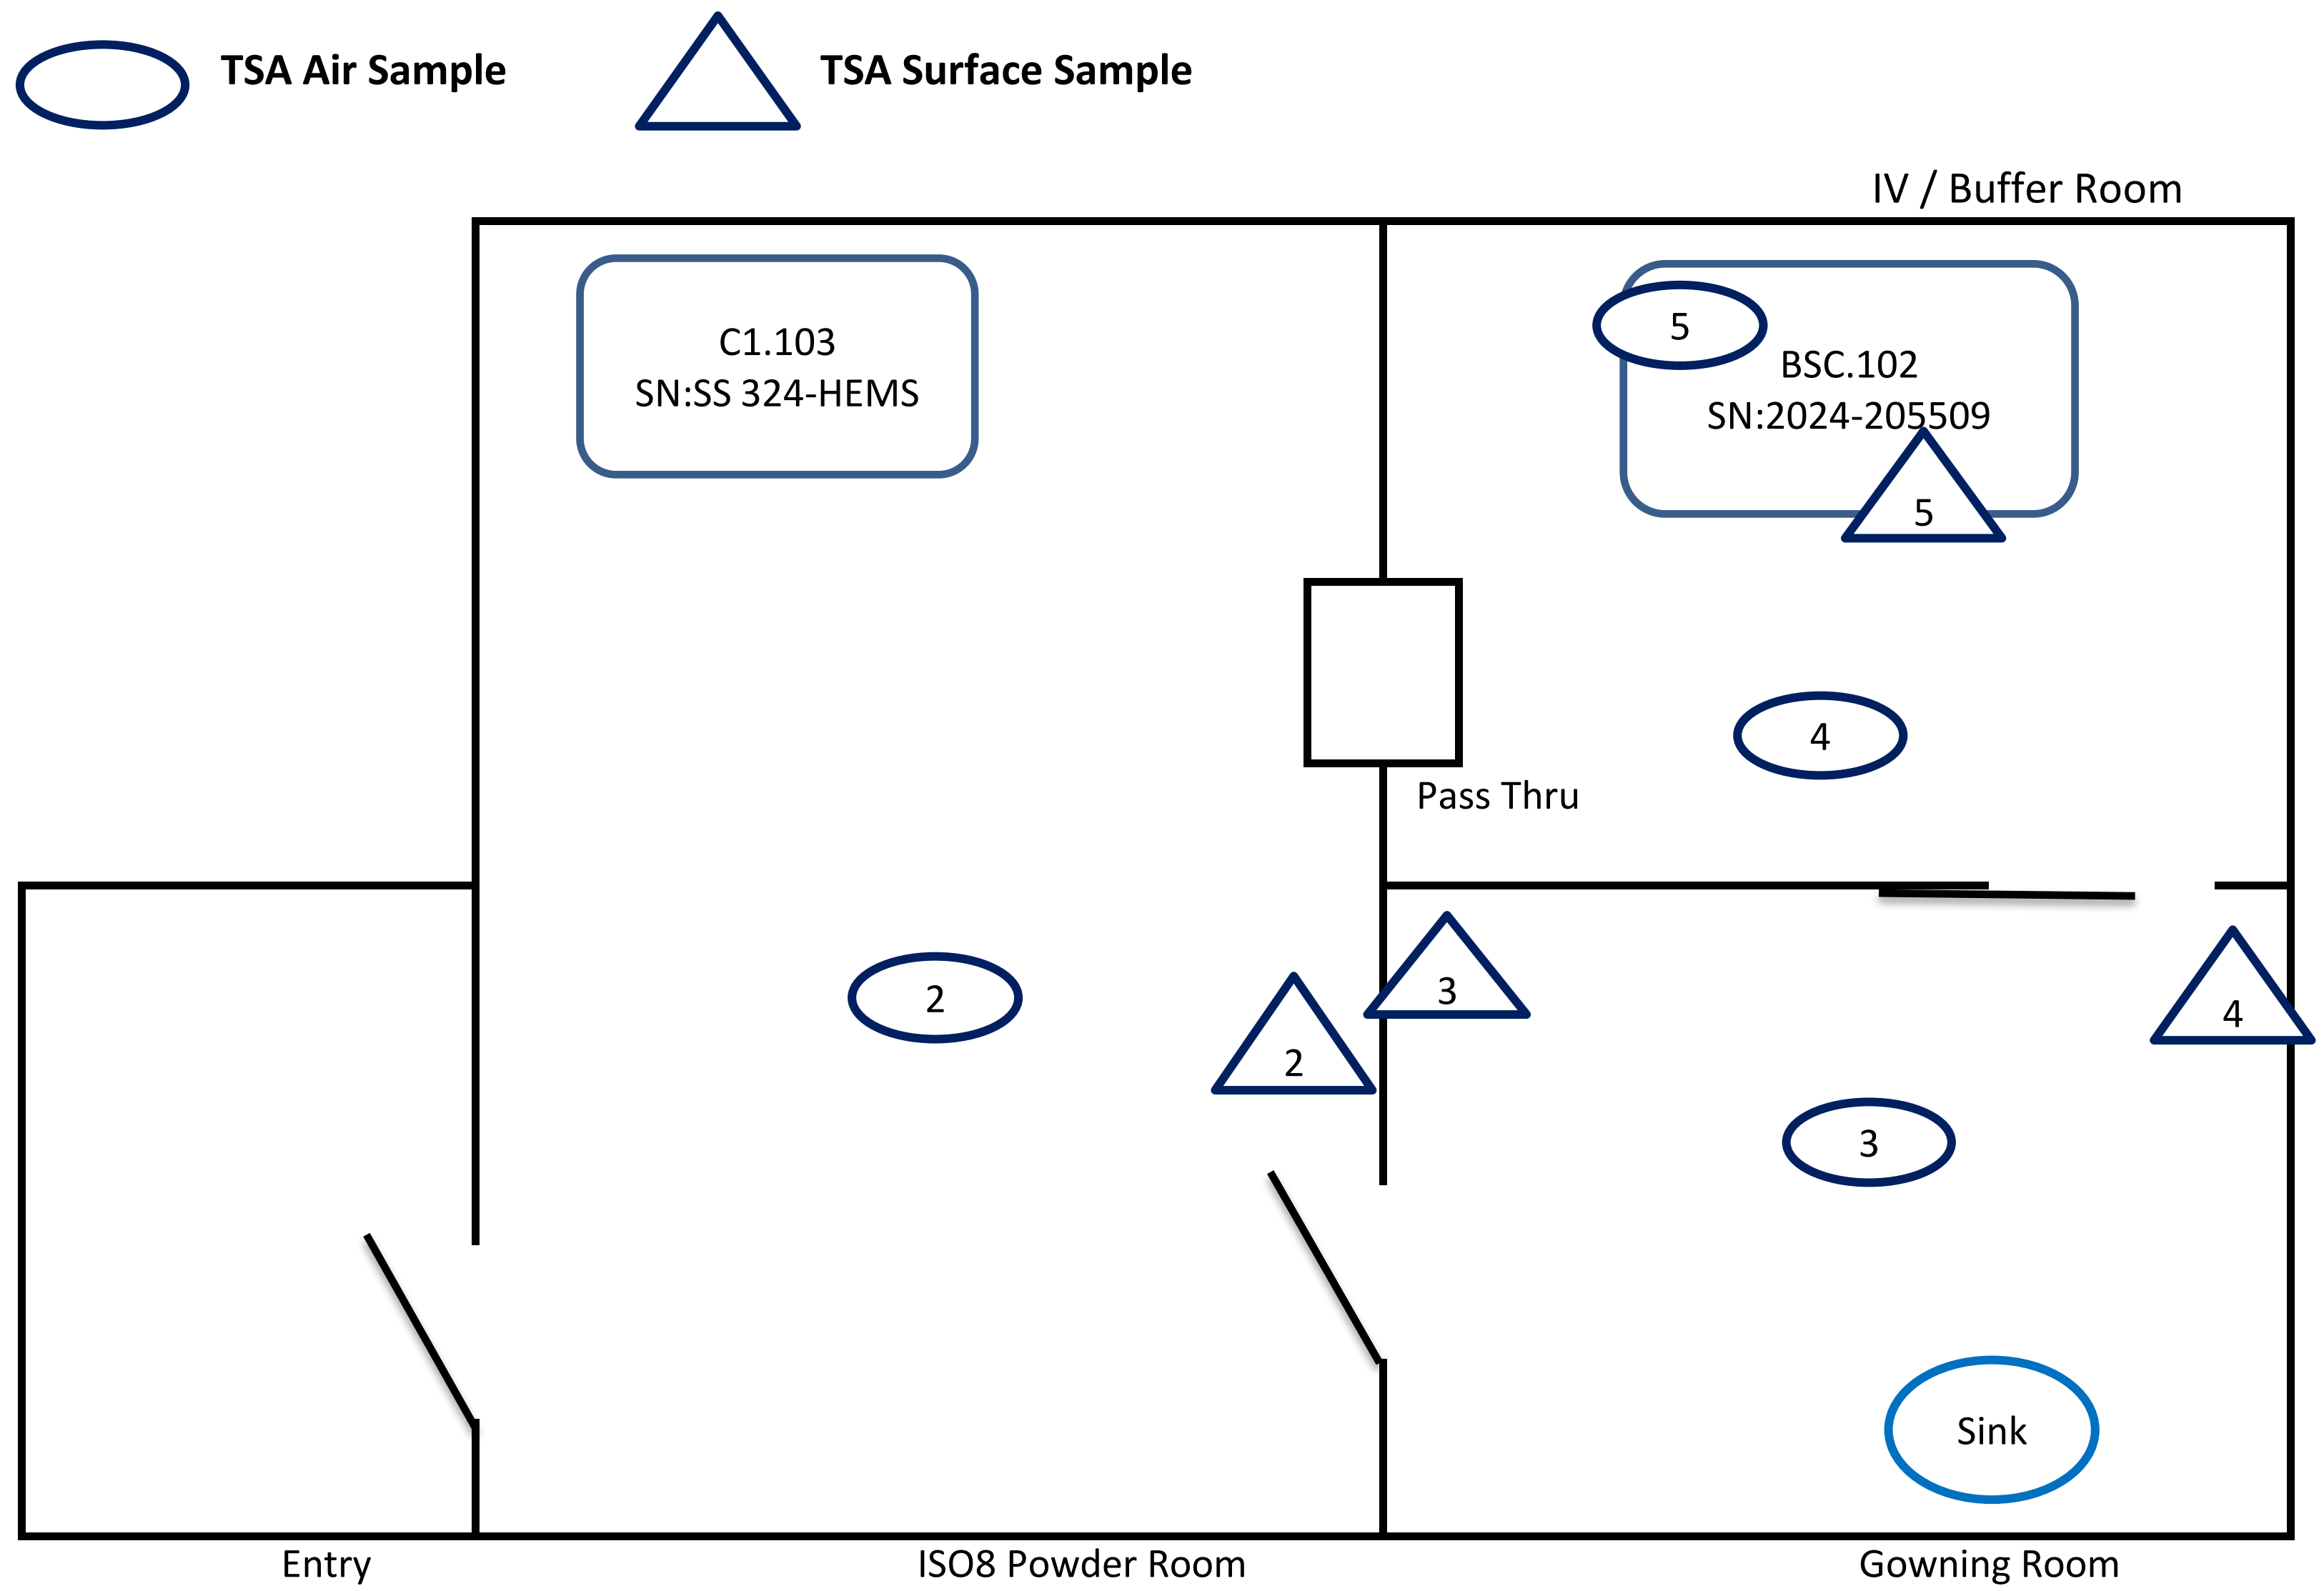

Room Dimensions
